


ID	Task Name	Duration	Start	Finish	Precedence	% Work Complete	Resource Initials	3rd Quarter			1st Quarter			3rd Quarter			Jan		Feb							
								Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	
1	Housing Replacement Analysis Project	275 days?	Mon 10/31/11	Wed 11/28/12		25%		[Gantt bars for 1-16]																		
2	Project Kickoff Meeting	1 day	Mon 10/31/11	Mon 10/31/11		100%		[Gantt bar for 2]																		
3	Discovery Phase (as-is)	186 days?	Fri 11/4/11	Wed 8/1/12		66%		[Gantt bars for 3-15]																		
4	Business Justification	20 days	Fri 11/4/11	Tue 12/6/11		100%		[Gantt bar for 4]																		
5	Write Business Justification	10 days	Mon 11/14/11	Fri 11/25/11		100%	JM	[Gantt bar for 5]																		
6	Review Business Justification	6 days	Fri 11/11/11	Fri 11/11/11		100%	JM	[Gantt bar for 6]																		
7	Obtain Approval from Project Team	1 day	Tue 11/29/11	Tue 11/29/11	5,6	100%	JM	[Gantt bar for 7]																		
8	Obtain Approval from Project Sponsors	0 days	Tue 12/6/11	Tue 12/6/11	7	100%	JM	[Gantt bar for 8]																		
9	Business Justification completed	0 days	Tue 12/6/11	Tue 12/6/11	8	100%	JM	[Gantt bar for 9]																		
10	Project Scope Document	19 days	Mon 11/7/11	Tue 12/6/11		100%		[Gantt bars for 10-15]																		
11	Write Project Scope Document	5 days	Mon 11/7/11	Fri 11/11/11		100%	JM	[Gantt bar for 11]																		
12	Review Project Scope Document	1 day	Fri 11/18/11	Fri 11/18/11	11	100%	JM	[Gantt bar for 12]																		
13	Obtain Approval from Project Team	1 day	Tue 11/29/11	Tue 11/29/11		100%	JM	[Gantt bar for 13]																		
14	Obtain Approval from Project Sponsors	0 days	Tue 12/6/11	Tue 12/6/11		100%	JM	[Gantt bar for 14]																		
15	Project Scope completed	0 days	Tue 12/6/11	Tue 12/6/11		100%	JM	[Gantt bar for 15]																		
16	Discovery Meetings	125 days	Thu 12/15/11	Thu 6/14/12	4,10	100%		[Gantt bar for 16]																		
17	Housing / Lottery	94 days	Thu 12/15/11	Wed 5/2/12		100%		[Gantt bar for 17]																		
18	Freshman (new to the Institute)	2 days	Thu 12/15/11	Fri 12/16/11		100%	RR	[Gantt bar for 18]																		
19	Upperclassman	1 day	Mon 4/9/12	Mon 4/9/12		100%	RR	[Gantt bar for 19]																		
20	Graduate Students	1 day	Wed 5/2/12	Wed 5/2/12		100%	JS	[Gantt bar for 20]																		
21	Housing filemaker Databases	10 days	Mon 2/6/12	Fri 2/17/12		100%		[Gantt bars for 21-37]																		
22	Master Blaster	5 days	Mon 2/6/12	Fri 2/10/12		100%	JS	[Gantt bar for 22]																		
23	UG Confirmation	5 days	Mon 2/6/12	Fri 2/10/12		100%	RR	[Gantt bar for 23]																		
24	Conference / Guest	5 days	Mon 2/6/12	Fri 2/10/12		100%	RR	[Gantt bar for 24]																		
25	Vacancy	5 days	Mon 2/13/12	Fri 2/17/12		100%	JS	[Gantt bar for 25]																		
26	Early Return	5 days	Mon 2/13/12	Fri 2/17/12		100%	RR	[Gantt bar for 26]																		
27	Waiting List	5 days	Mon 2/13/12	Fri 2/17/12		100%	JS	[Gantt bar for 27]																		
28	Front Desk	5 days	Mon 2/13/12	Fri 2/17/12		100%	RR	[Gantt bar for 28]																		
29	Housing SISTIM Functionality on Housing	8 days	Tue 2/21/12	Thu 3/1/12		100%	RR	[Gantt bar for 29]																		
30	Housing MITSIS Functionality on Housing	8 days	Tue 2/21/12	Thu 3/1/12		100%	JS	[Gantt bar for 30]																		
31	Housing Stakeholder - HFS Accounting	5 days	Mon 3/5/12	Fri 3/9/12	30FS	100%		[Gantt bar for 31]																		
32	Discuss systems/applications/process	5 days	Mon 3/5/12	Fri 3/9/12		100%	JS	[Gantt bar for 32]																		
33	Discuss process calendar	5 days	Mon 3/5/12	Fri 3/9/12		100%	JS	[Gantt bar for 33]																		
34	Walkthrough of digital Building/Room S	5 days	Mon 3/5/12	Fri 3/9/12		100%	JS	[Gantt bar for 34]																		
35	Walkthrough of Room Rate Codes Set	5 days	Mon 3/5/12	Fri 3/9/12		100%	JS	[Gantt bar for 35]																		
36	Analysis/review of OTF process	5 days	Mon 3/5/12	Fri 3/9/12		100%	JS	[Gantt bar for 36]																		
37	Discuss functionality/efficiency/informa	5 days	Mon 3/5/12	Fri 3/9/12		100%	JS	[Gantt bar for 37]																		
38	Housing Stakeholder - Student Financial	5 days	Tue 3/13/12	Mon 3/19/12	31FS	100%		[Gantt bar for 38]																		
39	Assess primary users/roles	5 days	Tue 3/13/12	Mon 3/19/12		100%	RR	[Gantt bar for 39]																		
40	Discuss systems/process flow	5 days	Tue 3/13/12	Mon 3/19/12		100%	RR	[Gantt bar for 40]																		
41	Discuss process calendar	5 days	Tue 3/13/12	Mon 3/19/12		100%	RR	[Gantt bar for 41]																		
42	Housing Stakeholder - Registrar	5 days	Wed 3/21/12	Tue 3/27/12	38FS	100%		[Gantt bar for 42]																		
43	Evaluate scope of affected data/proces	5 days	Wed 3/21/12	Tue 3/27/12		100%	JS	[Gantt bar for 43]																		
44	Examine dataflow for MITSIS Directory	5 days	Wed 3/21/12	Tue 3/27/12		100%	JS	[Gantt bar for 44]																		
45	Examine current supporting processes	5 days	Wed 3/21/12	Tue 3/27/12		100%	JS	[Gantt bar for 45]																		
46	Housing Stakeholders - Card Office / SEMC	1 day	Fri 3/23/12	Fri 3/23/12		100%	RR	[Gantt bar for 46]																		
47	Housing Stakeholders - Campus Dining	1 day	Wed 4/4/12	Wed 4/4/12		100%	RR	[Gantt bar for 47]																		
48	Housing Stakeholders - Tech Cash	1 day	Wed 4/4/12	Wed 4/4/12		100%	JS	[Gantt bar for 48]																		
49	UG House Managers	1 day	Thu 4/12/12	Thu 4/12/12		100%	RR	[Gantt bar for 49]																		
50	GRAD House Managers	1 day	Tue 4/17/12	Tue 4/17/12		100%	JS	[Gantt bar for 50]																		
51	Housing Stakeholders - Card Office / SEMC	1 day	Mon 4/23/12	Mon 4/23/12		100%	JS	[Gantt bar for 51]																		
52	Dean On Call	1 day	Thu 6/14/12	Thu 6/14/12		0%		[Gantt bar for 52]																		
53	FSILG	1 day	Tue 5/15/12	Tue 5/15/12		100%	JS	[Gantt bar for 53]																		
54	Discovery Phase Documentation	80 days?	Mon 4/9/12	Fri 7/27/12		23%		[Gantt bar for 54]																		
55	As-Is Business Process Descriptions	45 days?	Mon 4/9/12	Fri 6/8/12		45%		[Gantt bar for 55]																		
56	Undergraduate Process	45 days	Mon 4/9/12	Fri 6/8/12		39%		[Gantt bar for 56]																		
57	Undergraduate Process - Internal	15 days	Mon 4/9/12	Fri 4/27/12		100%	RR	[Gantt bar for 57]																		
58	Present Undergraduate Draft Vers	1 day	Fri 5/4/12	Fri 5/4/12	57,62	100%	RR	[Gantt bar for 58]																		
59	Undergraduate Process - Word D	23 days	Mon 5/7/12	Wed 6/6/12	58	0%	RR	[Gantt bar for 59]																		
60	Present Undergraduate Process -	1 day	Fri 6/8/12	Fri 6/8/12	59	0%	RR	[Gantt bar for 60]																		
61	Obtain approval from Project Spo	0 days	Fri 6/8/12	Fri 6/8/12	60	0%	JM	[Gantt bar for 61]																		
62	Graduate Process	44 days?	Mon 4/9/12	Fri 6/8/12		50%	JS	[Gantt bar for 62]																		
63	Graduate Process - Internal review	15 days	Mon 4/9/12	Fri 4/27/12		100%	JS	[Gantt bar for 63]																		
64	Present Graduate Draft Version to	1 day	Mon 5/21/12	Mon 5/21/12	63	100%	JS	[Gantt bar for 64]																		
65	Graduate Process - Word Docum	1 day	Mon 5/21/12	Mon 5/21/12		100%	JS	[Gantt bar for 65]																		
66	Present Graduate Process - Word	1 day?	Tue 5/22/12	Tue 5/22/12	63,65	100%	JS	[Gantt bar for 66]																		
67	Obtain approval from Project Spo	0 days	Fri 6/8/12	Fri 6/8/12	66	0%	JM	[Gantt bar for 67]																		
68	As-Is Business Process Documentation	0 days	Fri 6/8/12	Fri 6/8/12	67	0%	RR,JS	[Gantt bar for 68]																		
69	As-Is Process Maps (Visual Micrografax F	42 days	Mon 5/7/12	Tue 7/3/12	58	8%		[Gantt bar for 69]																		

Project: HRA Project Plan
Date: Tue 6/5/12

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary		Deadline	

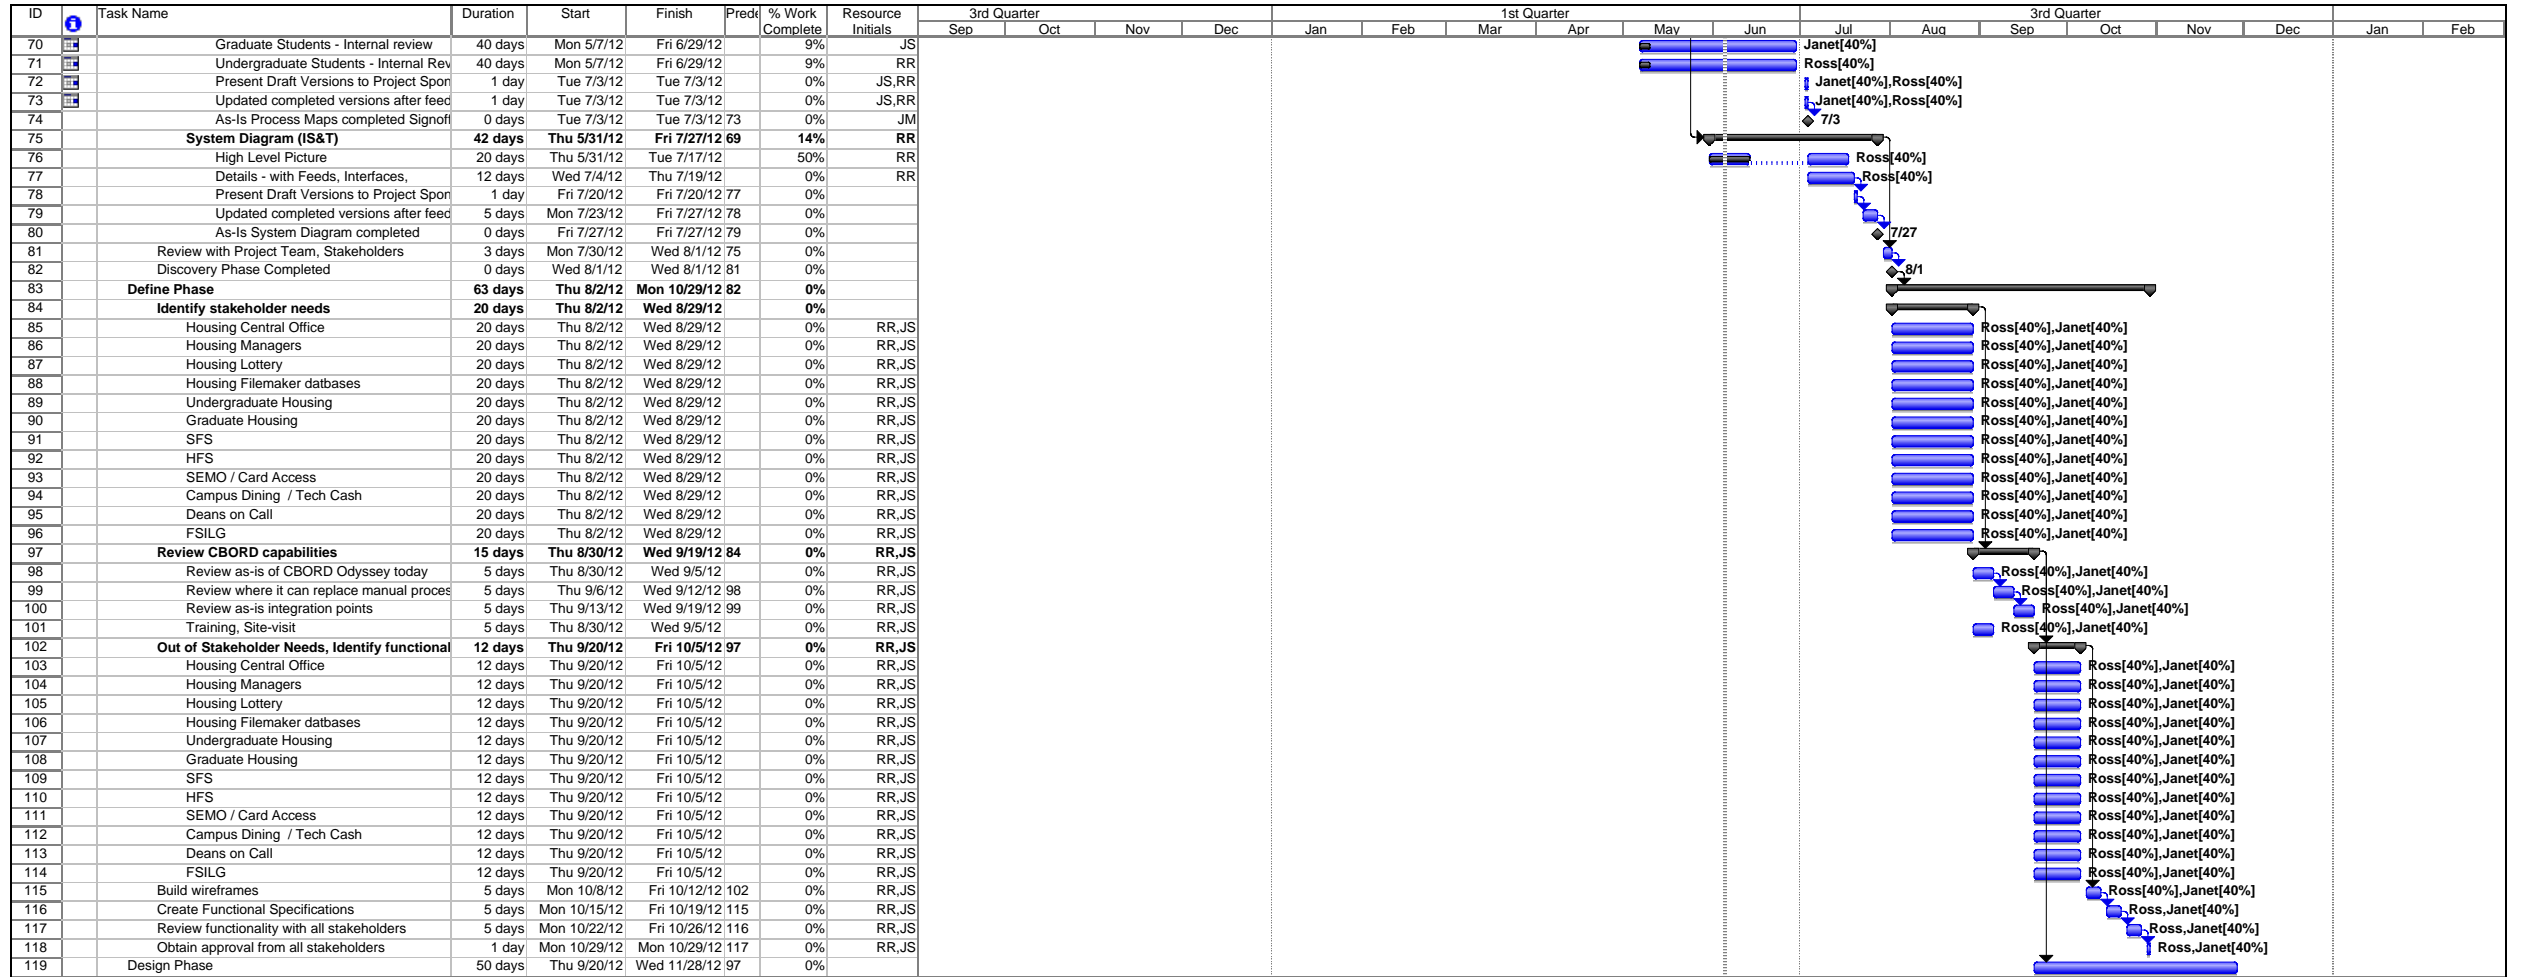

Project: HRA Project Plan Date: Tue 6/5/12	Task	Milestone	Roll Up Task	Roll Up Progress	External Tasks	Group By Summary
Progress	Summary	Roll Up Milestone	Split	Project Summary	Deadline	
